


## WORKED EXAMPLE

Jack Mo reads it aloud

# Fast-track structure

THE UNTRAINED EYE vs THE RISK MANAGER'S EYE

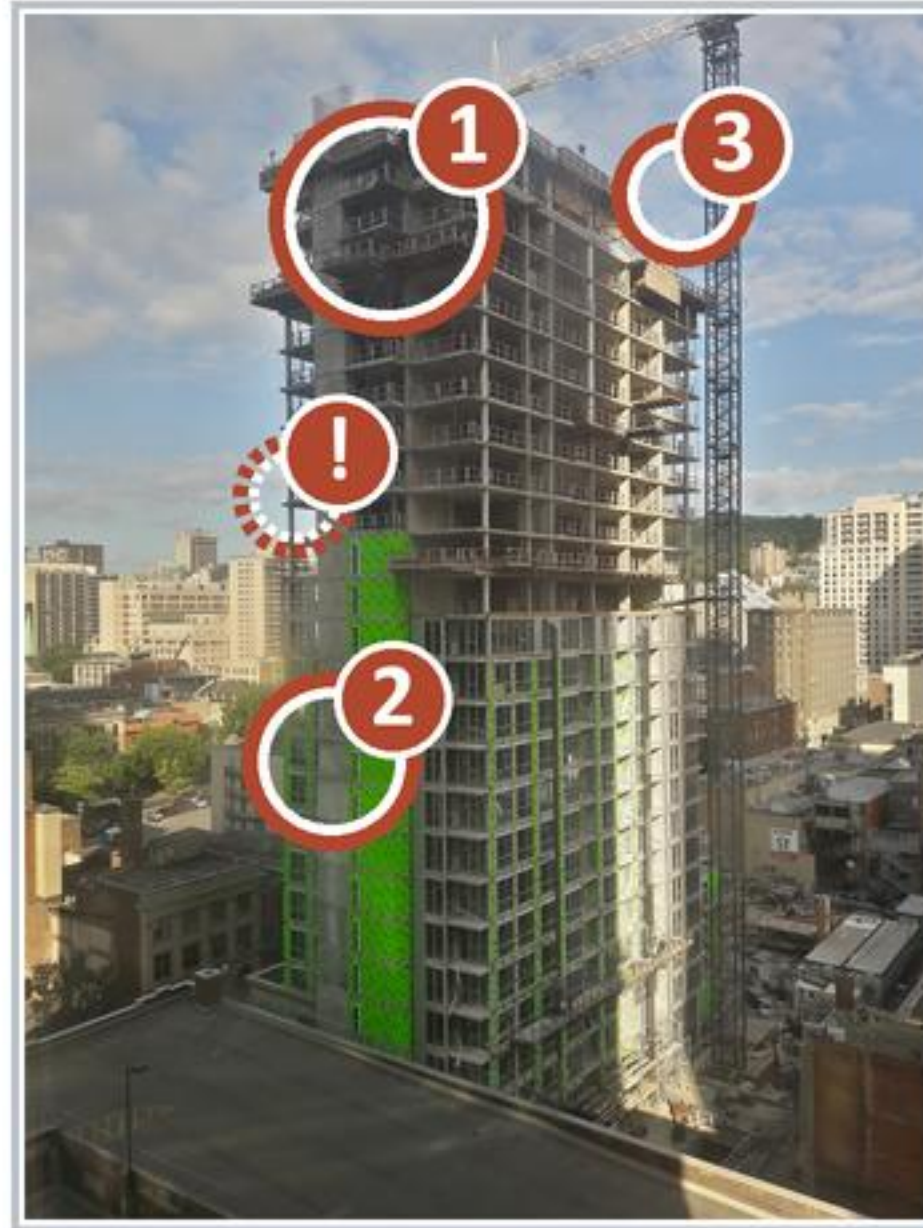

Jack Mo circles what his eye lands on — and the one thing that should be there and isn't.

To a passing eye this is a triumph — a tower shooting up so fast the cladding can barely keep pace, green glass crawling up floors while the bare gray frame already crowns the skyline. Progress you can measure by the week. A risk manager reads the same photo and feels the pace as a warning, not a win. They don't see speed; they see a structure that has outrun its own drawings. The casual eye sees finished floors below and new floors above and calls it momentum. The trained eye sees the gap between them and asks what the designers upstairs haven't decided yet — because this is a fast-track job, where design and construction run side by side, and the paper is still being drawn while the concrete is already poured. That gap is where the addenda live. A revision lands, and it changes work already standing on the lower floors — so it comes out, and goes back in, the right way this time. Push to win back the days, and the overtime climbs. Miss the contract date, and the penalty starts counting in money per day. The casual eye counts floors and feels reassured. The trained eye counts floors and braces for the corrections still in transit. The scene did not change between those two readings. The eye did. An untrained eye sees a building rising; a risk manager sees what each unfinished decision could undo, to whom, and when.

**THIS SCENE FEEDS YOUR REGISTER**

R30 • R34 • R38 • R42 • R46 — the five students dealt this scene.



## The discipline under that read

The moves you run so you can see it too — then five register rows fall out of one glance.

|                                                                             |                                                                                                                                                                                                                                                                                                                                                    |
|-----------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <b>LOOK</b>                                                                 | sweep overhead → working level → ground/openings → edges → background (don't lock on the obvious).                                                                                                                                                                                                                                                 |
| <b>SPLIT</b>                                                                | say what you SEE — facts only: A bare gray concrete frame topping out near the crane while the floors below are already being clad, Green-tinted glazing climbing the mid-lower floors — finishes chasing a structure that is still growing, A single tower crane still feeding the top, meaning the structure is being built ahead of completion. |
| <b>NOTICE</b>                                                               | circle the cues: Bare frame racing ahead of the clad floors below; Green glazing climbing into a still-growing tower; The vertical seam between enclosed and open floors — and the missing No finished top-out and no complete drawing set on site — the design isn't done, so the building is rising ahead of the paper that defines it.          |
| <b>ASK → PROJECT</b>                                                        | what releases it, who's in the path, what happens next — and in which phase.                                                                                                                                                                                                                                                                       |
| <b>NAME · five rows, born from one glance (cause → event → consequence)</b> |                                                                                                                                                                                                                                                                                                                                                    |

### 1 Changing drawings

Because design and construction are running at the same time on this fast-track job, a revised drawing may change work already installed on the lower floors, leading to that work being torn out and rebuilt.

Owner: Project Manager · Trigger: a new addendum or revised drawing logged after the affected floor was already poured or clad

### 2 Baseline / schedule

Because the structure is racing ahead on a schedule this fast, milestones may slip unnoticed against the baseline, leading to a delivery date that quietly moves out before anyone reacts.

### 3 LD penalties

Because the contract date is fixed while the pace eats the float, the job may miss that date, leading to liquidated damages charged in money for every day late.

### 4 Build-wrong

Because crews are building ahead of a finished design, a floor may be built to a drawing that later changes, leading to correct-looking work that must be demolished and reinstalled as rework.

### 5 Acceleration

Because the team pushes to recover the days lost to revisions, overtime and added crews may be thrown at the work, leading to acceleration cost on top of the original budget.

### READING MOVE · bank this card

“Ask what the structure has gotten ahead of — when the building races ahead of the paper, expect the paper to catch up the hard way, as rework.”

### SUCCESS CARD · check the read against these six

- ☐ a real, visible cue
- ☐ cause is a site condition
- ☐ a future event
- ☐ consequence on cost/time/quality/safety
- ☐ owner + early-warning trigger
- ☐ (M4) P and I each defended

P × I? Not yet — Module 2 IDENTIFIES; Module 4 ASSESSES. These rows seed register rows R30 · R34 · R38 · R42 · R46.
